

National Broadband Plan Project Status

Kilkenny County Council


TJ Malone, Chief Executive, NBI Deployment

21st February 2022

The National Broadband Plan

The National Broadband Plan (NBP) is the largest ever telecommunications project undertaken by the Irish State.

It aims to radically transform the country's broadband landscape through the delivery of quality, affordable high-speed broadband to all parts of Ireland where such services are not available commercially.

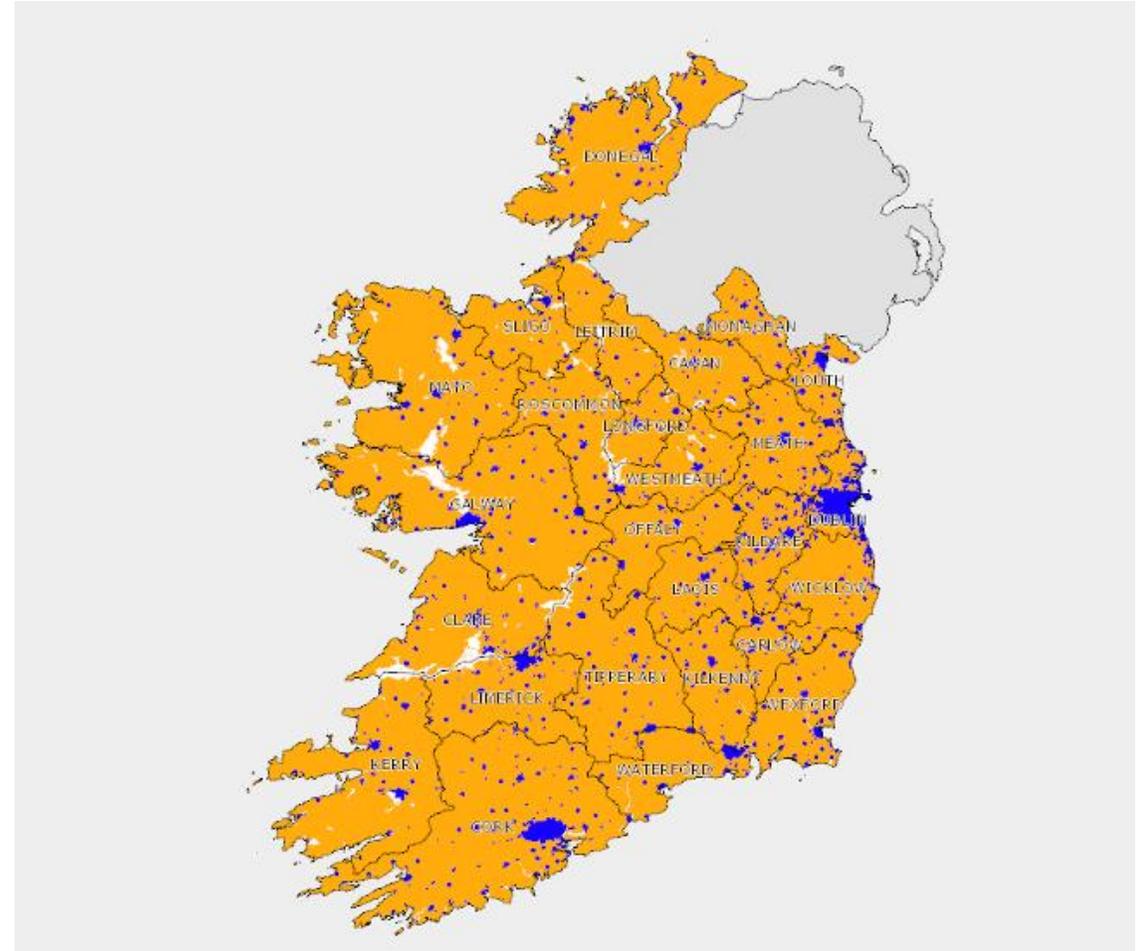

AMBER areas - the target areas for the State intervention of the National Broadband Plan

BLUE areas - where commercial operators are delivering or have indicated plans to deliver high speed broadband services.

The National Broadband Plan

Access Regardless of Geography

The NBP will ensure that all people and businesses have access to high-speed broadband, no matter where they live or work.

The Department of Communications identified all premises in the country that don't have access to high-speed broadband – this is called the Intervention Area.

554,000 + Premises

NBI have been contracted to connect the 554,000+ premises **ensuring no one is left behind.**

The network is being designed, built and operated by National Broadband Ireland, using a combination of State subsidy and commercial investment.

7 Year Build Programme

It's a 7-year build programme – currently scheduled to complete in 2026.

NBI are responsible for the management and maintenance of the NBI™ network for the next 25 years.

The National Broadband Plan

National Overview

Premises Surveyed: 300,908

Designs Complete: 254,000

Constructed/under
construction: 154,088

Premises Available for
Order/Pre-Order: 54,512

Premises Connected: 6,966

Connections Pending: 1,307

RSP Contracts signed: 50

Total EOI's: 62,906

Public BCP's Installed: 270


Schools BCP's Installed: 216

The National Broadband Plan

Build Underway in 26 Counties

Premises Live in 18 Counties


Carlow	Kildare	Roscommon
Clare	Kilkenny	Sligo
Cavan	Laois	Tipperary
Cork	Limerick	Waterford
Galway	Louth	Wexford
Kerry	Monaghan	Wicklow

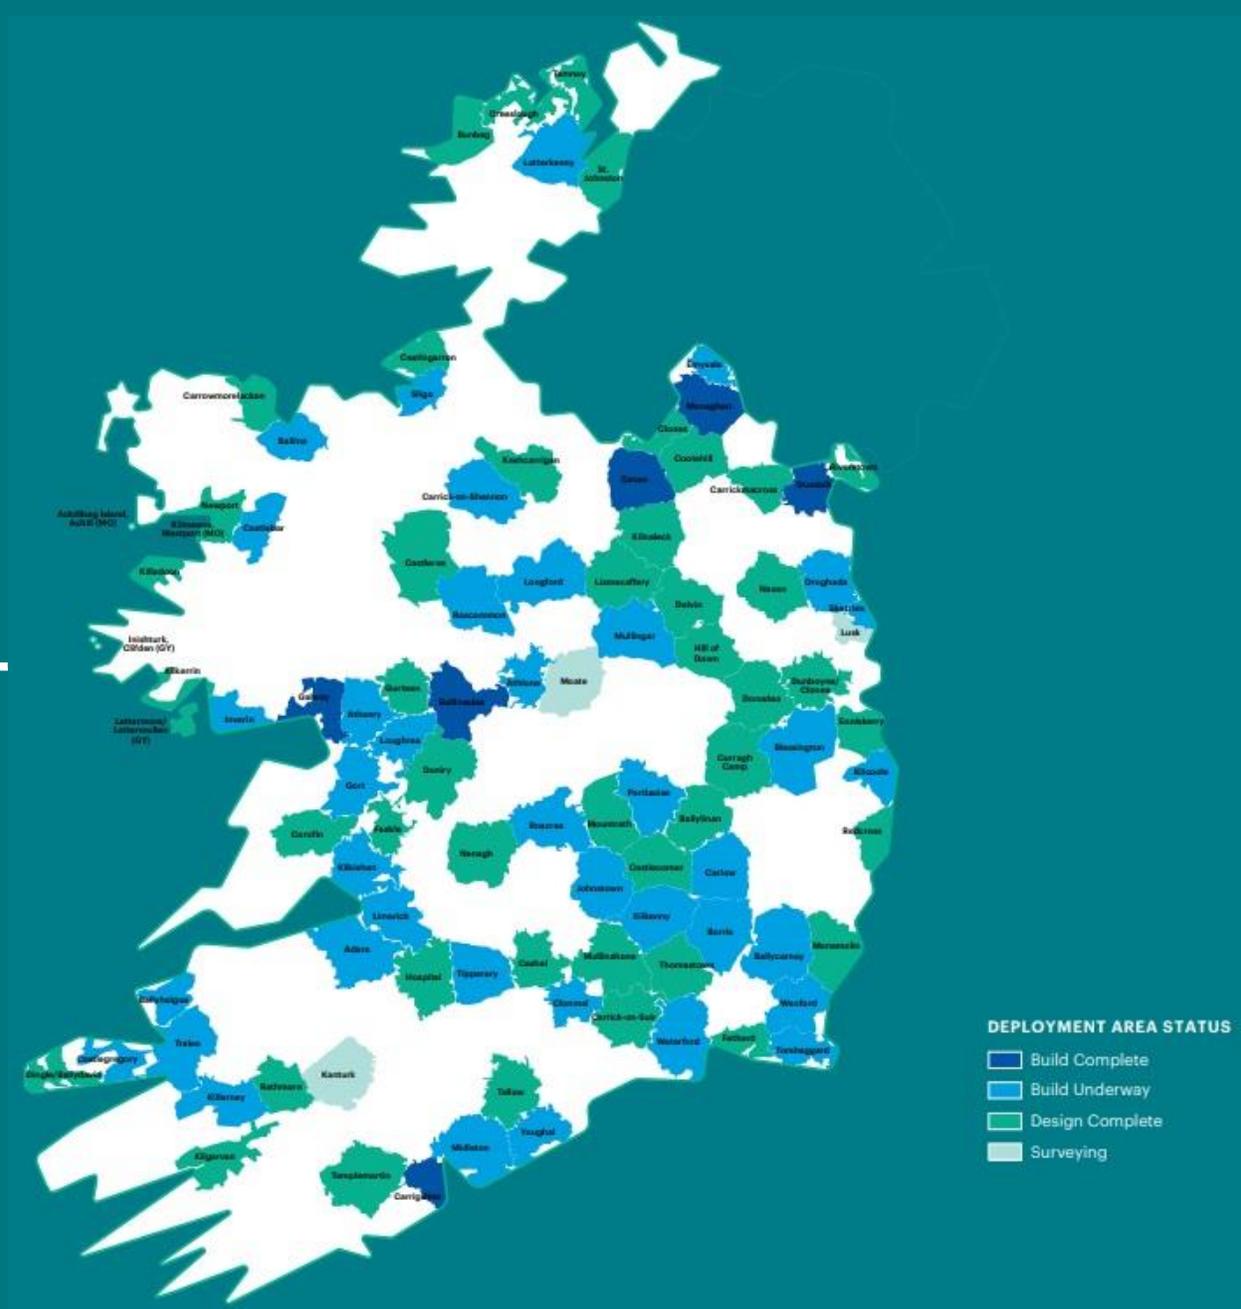

Activity Overview

Different Deployment Areas are at different stages of the construction cycle.

- **Engineering Surveys** of townlands are required to examine the existing pole and duct network for inclusion in the design, if any remedial works required and to determine what level of new network infrastructure is required.
- NBI's **Detailed Design** process confirms infrastructure, power & footprint required, drawings, openair works, Local Authority requirements, and revised cost analysis.
- **Network Build.** After the designs have been approved, pre-works, then main works start on the ground: readying existing infrastructure (openair), upgrading & adding poles and ducts, laying fibre, preparing backhaul facilities, fulfilling Local Authority requirements, tree trimming etc.

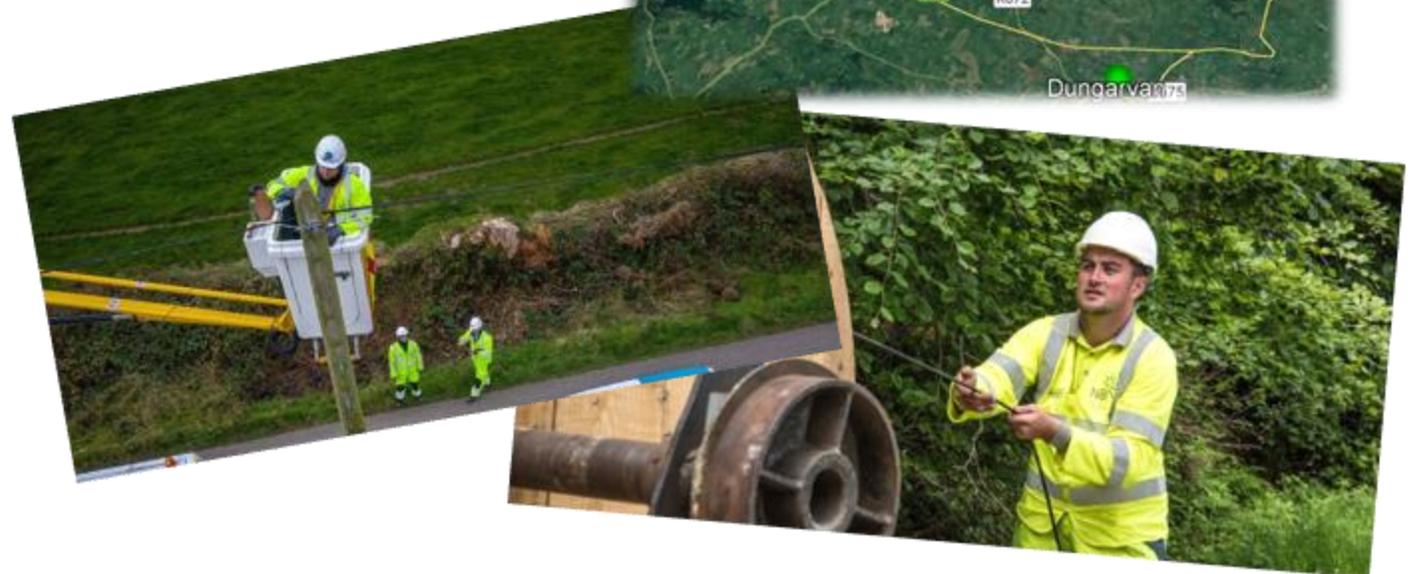

Infrastructure Upgrades



mitigate the risk of delay in consents from the various state agencies, and a process of engagements with

- Local Government Management Agency (LGMA)
- County and City Management Association (CCMA)
- Road Management Office (RMO)

The objective of these engagements was to establish a national set of guidelines for the erection of new telegraph poles to support the timely connection of premises.

Section 254

Specifically, Section 254 of Planning and Development Act is an important step for a successful rollout and NBI's ability to connect homes.

DHLG Circular
PL07/2021 18th August
2021

Prioritisation of license applications - In further recognition of the Governments priority commitment to ensure swift rollout of broadband throughout the county, planning authorities are requested to prioritize Section 254 license applications for overground cables, and to process these as speedily as possible.



OVERHEAD
89,454km

15,057km

UNDERGROUND



1,466,534

CABLING 142,384km

New guidelines were issued on 5th May 2021 to all Local Authorities to assist planners and engineers.

Working Together in Support of the NBP

- Kilkenny County Council will see significant activity from NBI and our subcontractors in terms of **licence applications**.
- Consistency of approach from **national guidelines** critical to efficient processing of licences and timely connection of premises so citizens have access to the high-speed broadband.
- **Broadband Officers** in each Local Authority play a key role in support of the project delivery.


Elected Representatives have important role in ensuring Local Authorities are working with all relevant stakeholders in ensuring smooth roll-out of National Broadband Plan.



Co. Kilkenny - Fibre to the Home

Co. Kilkenny Overview

- There are **~18,563** premises in Co. Kilkenny without access to high-speed broadband.
- This represents **38%** of the total premises in the county.
- Government will invest **~€72m** in delivering the NBP in Co. Kilkenny.
- **7** Broadband Connection Points (BCPs) and **21** schools are also in scope.

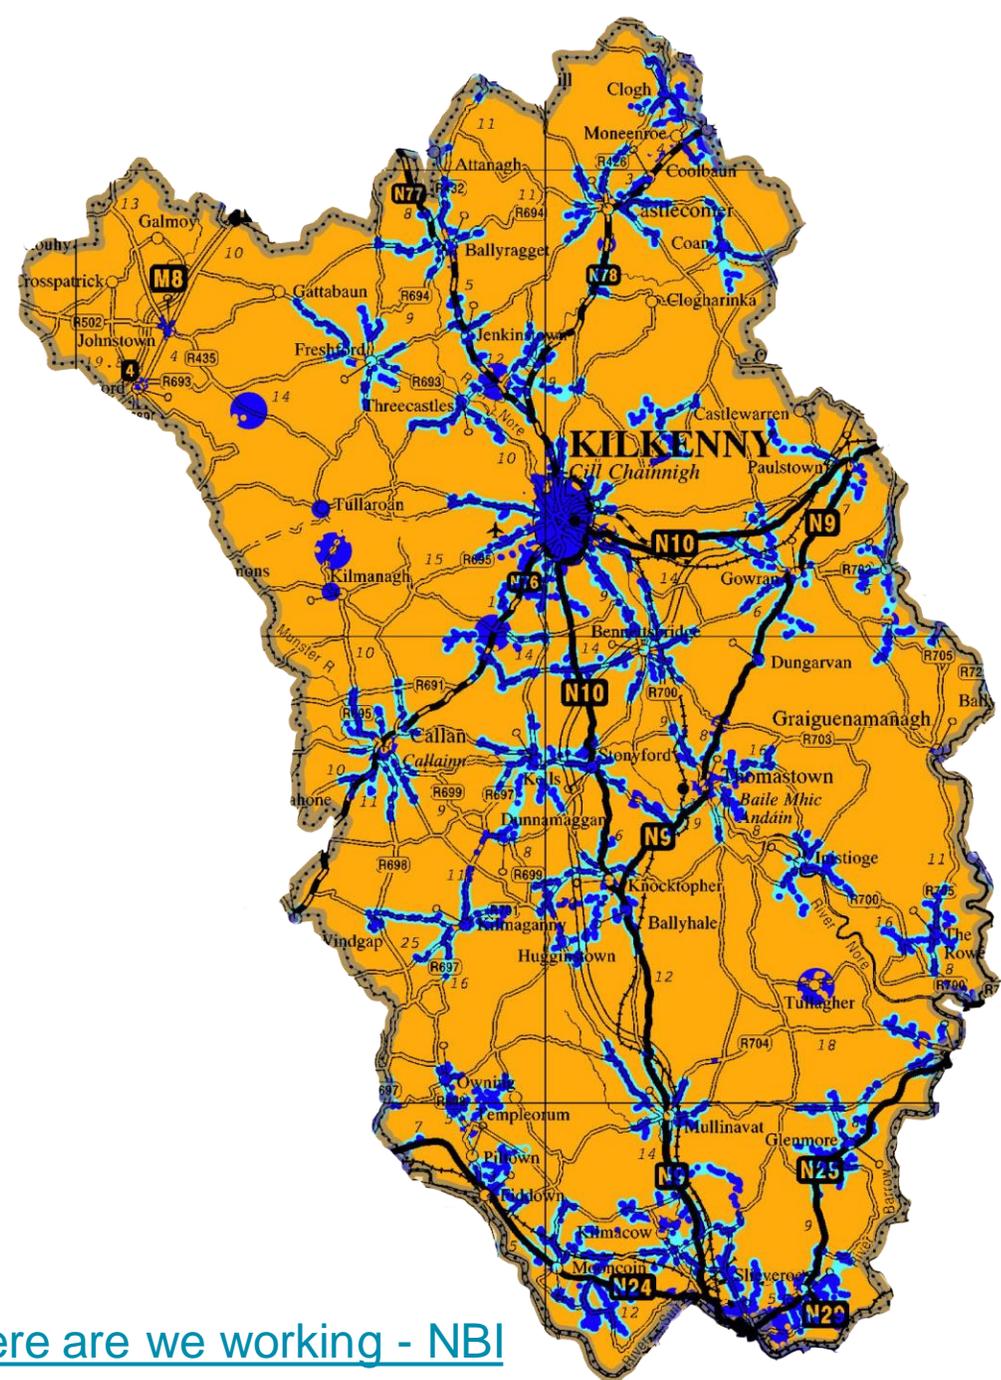

Kilkenny

- Total number of premises to be served in County Kilkenny: 18,563
- 100% of Kilkenny premises will be surveyed by end 2022
- 59% of Kilkenny premises will have build commenced by end 2022; 97% by end 2023
- 97% of Kilkenny premises will have build complete by end 2024

Kilkenny Surveys Completed


Build Commencing Profile

Build Complete Profile

2020	50%	2021	50%	2022	43%
2021	97%	2022	59%	2023	52%
2022	100%	2023	97%	2024	97%
		2024	100%	2025	100%

Waterford Deployment Area - includes premises in County Kilkenny


- Waterford Deployment Area serves **6,285 premises**, including **2,532 premises (40%)** in County Kilkenny
- Status: **Network Build in Progress**
- Timeline for connections: **Aug 22 - Oct 22**

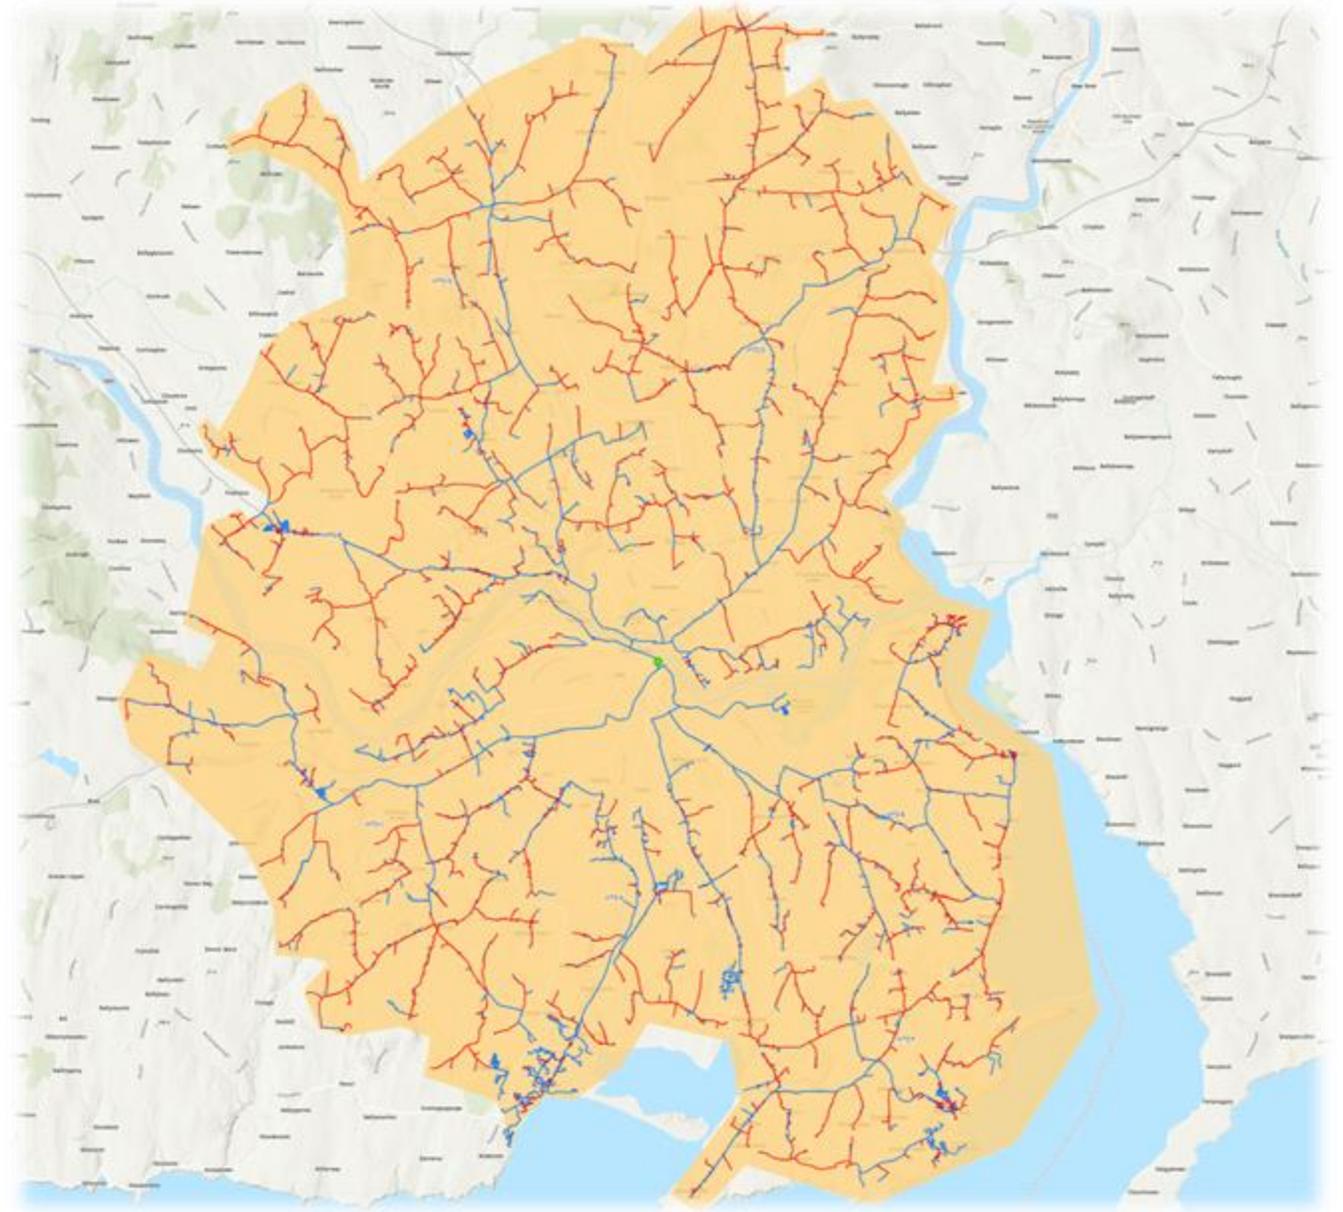

 Red lines, overhead infrastructure
 Blue line, underground infrastructure

Kilkenny Deployment Area


- Kilkenny Deployment Area serves **3,395 premises** in County Kilkenny
- Status: **Network Build in Progress**
- Timeline for connections: **Oct 22 - Jan 23**

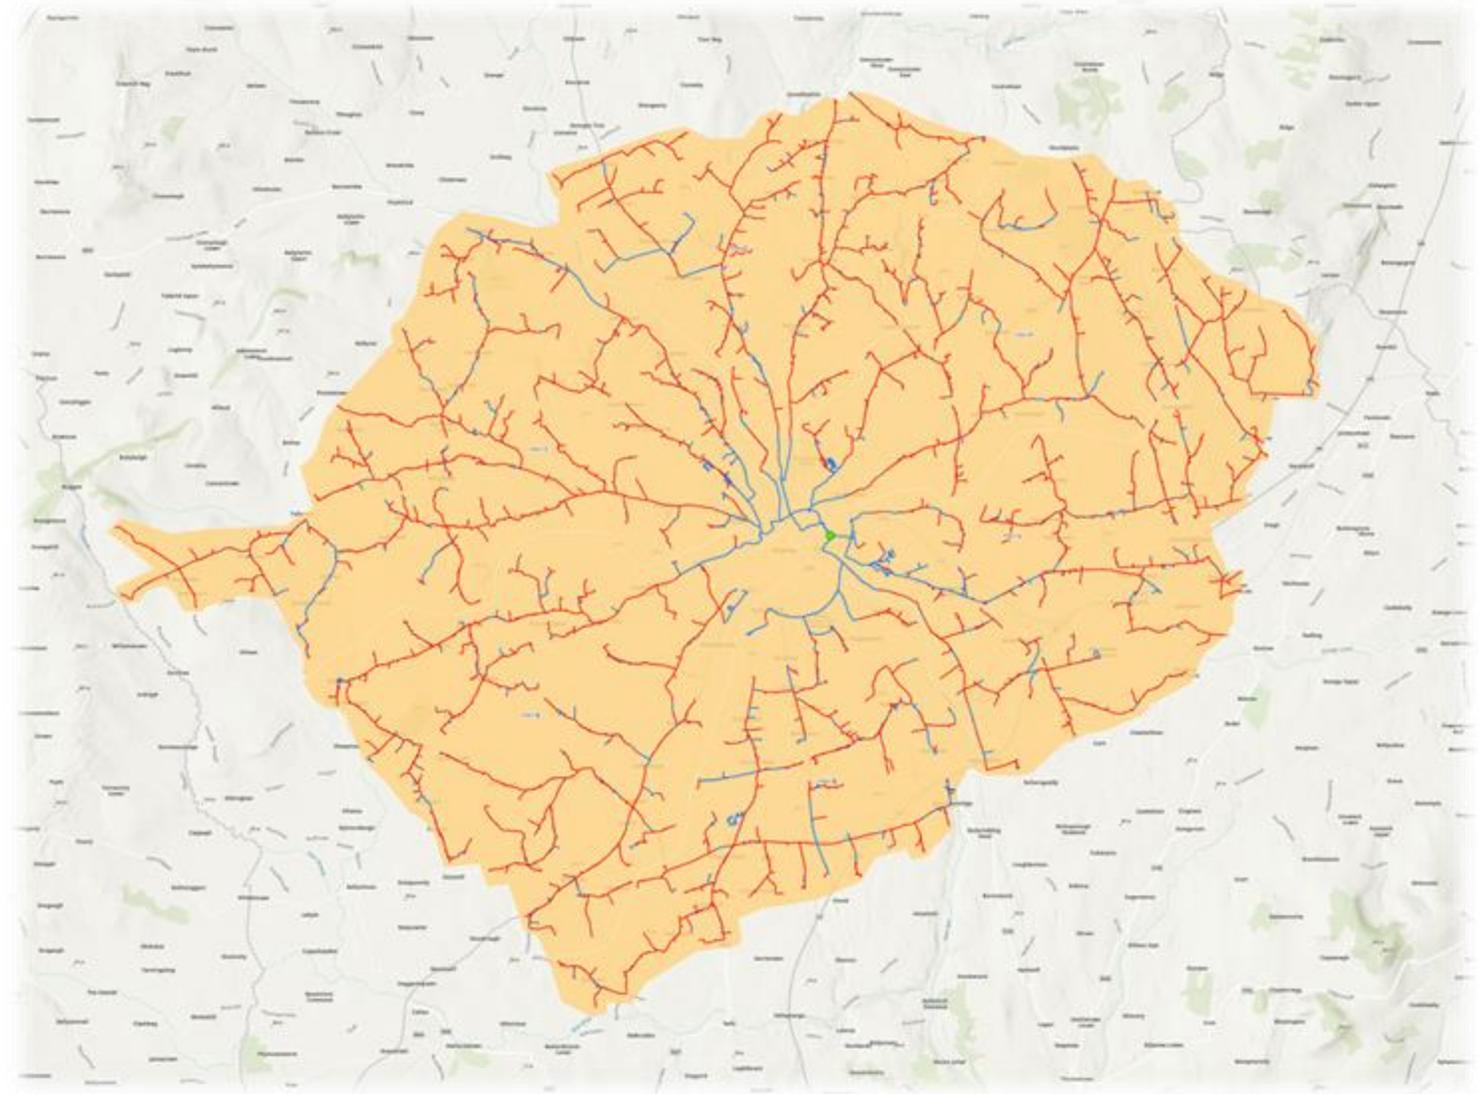

 Red lines, overhead infrastructure
 Blue line, underground infrastructure

Borris Deployment Area


- Borris Deployment Area serves **1,952 premises** in County Kilkenny
- Status: **Network Build in Progress**
- Timeline for connections: **Nov 22 - Jan 23**

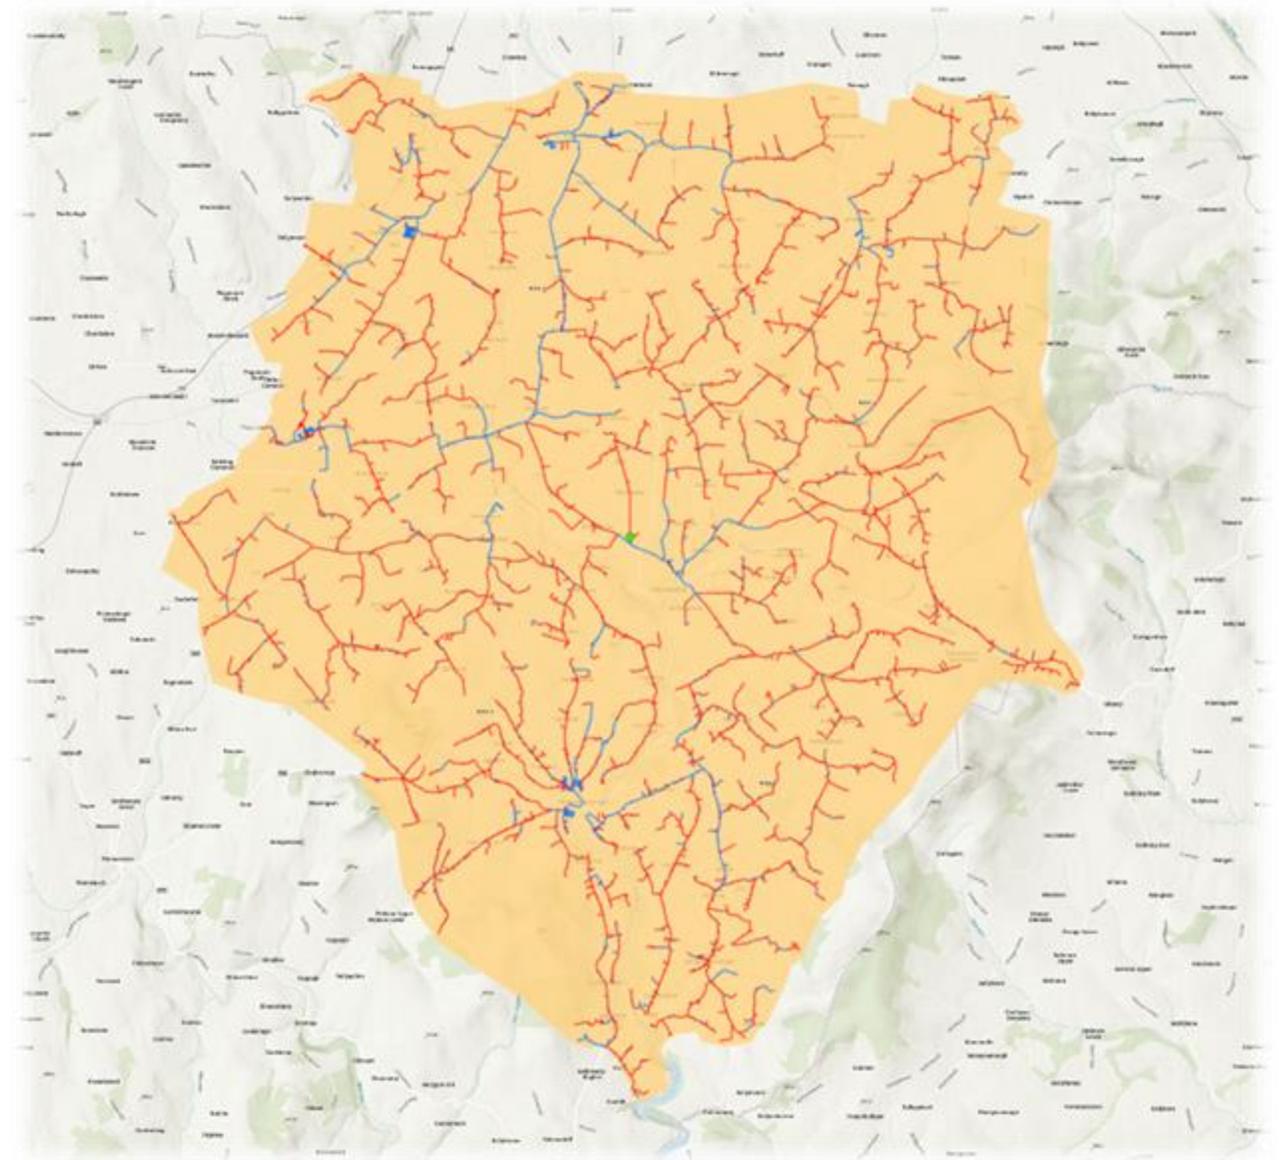

 Red lines, overhead infrastructure
 Blue line, underground infrastructure

Johnstown Deployment Area

- Johnstown Deployment Area serves **1,651 premises** in County Kilkenny
- Status: **Network Build in Progress**
- Timeline for connections: **Jan 23 - Mar 23**

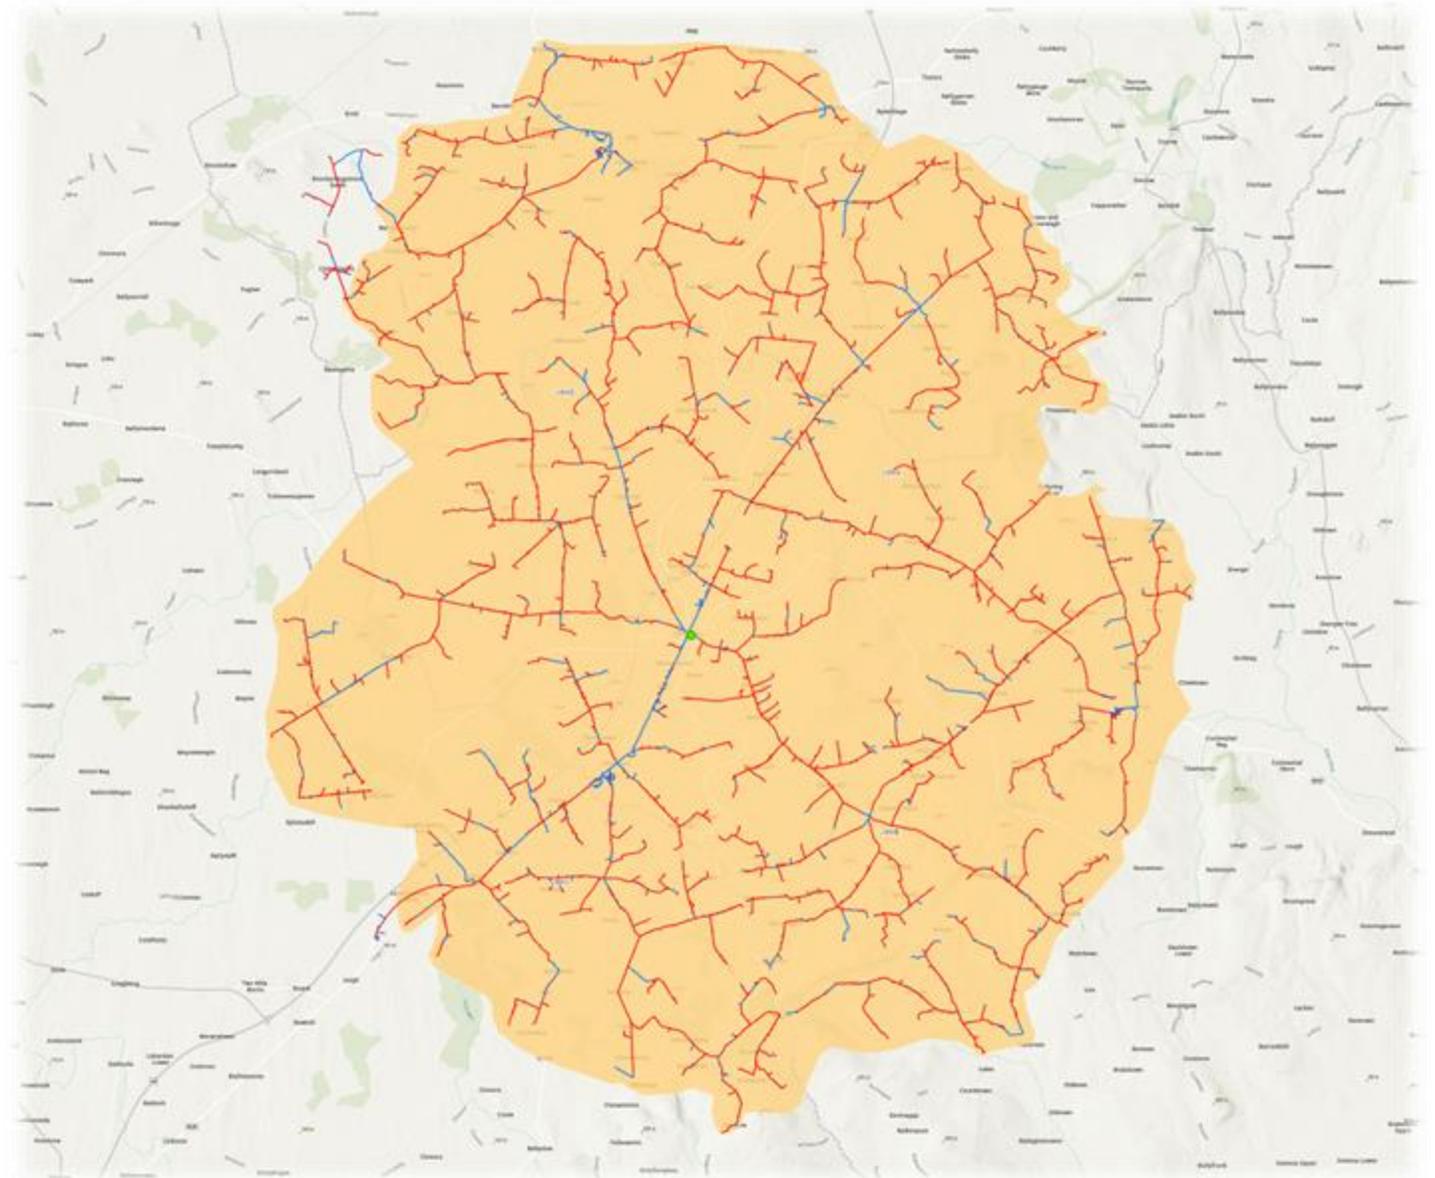

 Red lines, overhead infrastructure
 Blue line, underground infrastructure

County Kilkenny Deployment Areas

Deployment Area	# Premises in County Kilkenny	Status	Anticipated Date For Connection
Carlow*	50	Available To Order/Pre-Order	Available now
Waterford*	2532	Network Build in Progress	Aug 22 – Oct 22
Kilkenny	3395	Network Build in Progress	Oct 22 – Jan 23
Borris*	1952	Network Build in Progress	Nov 22 – Jan 23
Johnstown	1651	Network Build in Progress	Jan 23 – Mar 23
Castlecomer	2565	Survey Complete	Jan 23 – Dec 24
Carrick-On-Suir*	1537	Survey Complete	Jan 23 – Dec 24
Mullinahone*	1027	Survey Complete	Jan 23 – Dec 24
Thomastown	2679	Survey Complete	Jan 23 – Dec 24
Ballynabola*	541	Survey Pending	Jan 25 – Dec 26
Additional Premises	613	Survey Pending	Jan 25 – Dec 26

52% (9,580) of total premises in Kilkenny are currently under construction

These premises will be delivered between August 2022 and March 2023

*Deployment Areas in other counties serve premises in County Kilkenny

Co. Kilkenny - Broadband Connection Points & Schools


BCPs in County Kilkenny

7 **BCP** locations in County Kilkenny – all of which are now live.

The full list of BCPs is available on www.nbi.ie

BCPs for Connection	Phase
Galmoy Community Centre	Live
Crosspatrick Community Hall	Live
Graine Community Hall	Live
Ballyouskill Parish Hall	Live
Muckalee Handball Club	Live
Connolly's Pub	Live
Tullaghought Parish Hall	Live

BCPs are public locations which have been selected by the Local Authority / BBO's to receive high-speed connectivity in the early stages of the rollout.

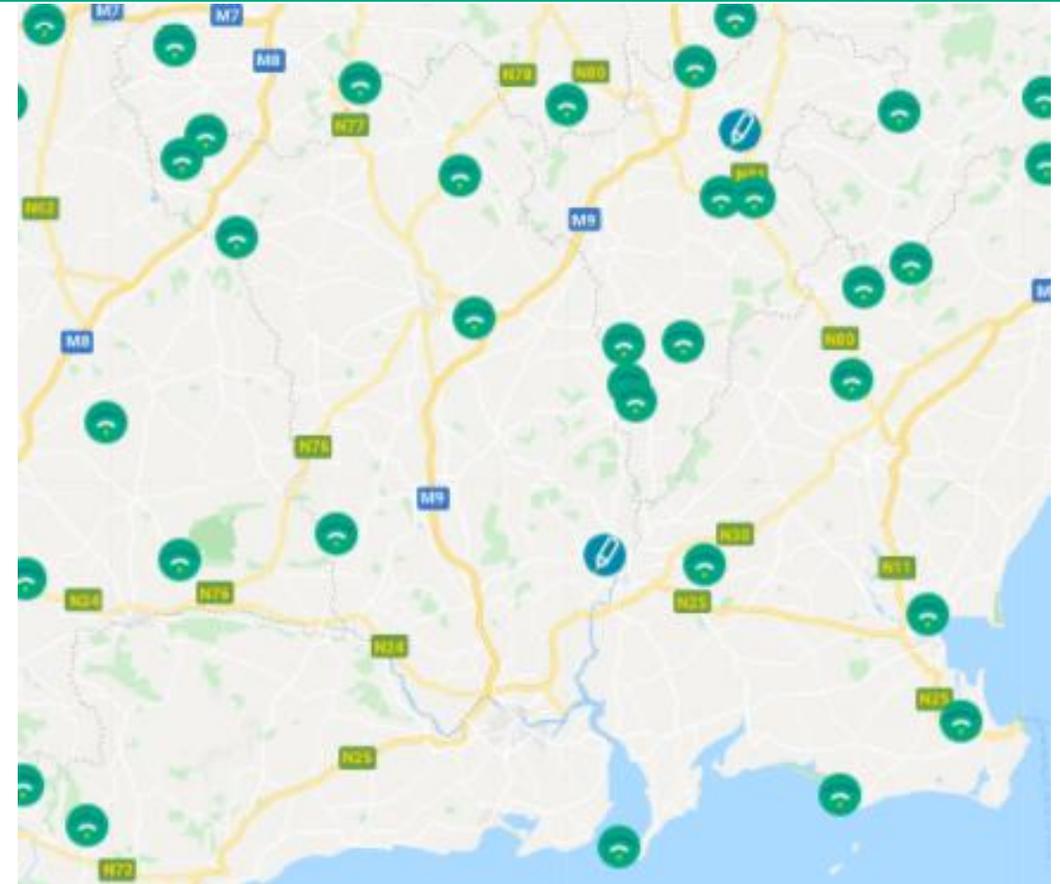

BCPs & Primary Schools in County Kilkenny

21 schools are in scope to connect to high-speed broadband:

The full list of BCPs is available on www.nbi.ie

Schools for Connection	Phase
SAINT AIDAN'S NATIONAL SCHOOL	Connected
LISTERLIN NATIONAL SCHOOL	Connected
CREENKILL NATIONAL SCHOOL	Connected
SAINT MICHAEL'S PRIMARY SCHOOL	Connected
SCOIL MHICHIL NAOFA	Connected
URLINGFORD NS	In Progress (Feb 22)
S N BAILE AN FHASAIGH	In Progress (Nov 22)
LISNAFUNCHINNS	Planned
S N SHEAN BHOTH	Planned
S N MHUIRE LOURDES BUAC	Planned
S N NAOMH COLMAIN	Planned
S N MUIRE	Planned

Schools for Connection	Phase
SCOIL BHRIDE B7C	Planned
S N BAILE AN PHIULL	Planned
BUNSCOIL MCAULEY RICE	Planned
S N MOIN RUADH MIXED	Planned
S N AN MOININ RUA	Planned
S N BHREANDAIN NAOFA	Planned
S N COLMAIN	Planned
S N CAISLEAN AN CUMAIR	Planned
HOLYCROSS N.S.	Planned

Functionality To Support Constituents

Eircode Search

Members of the public can easily determine if they are in the intervention area or not – via our Eircode search function.

www.nbi.ie



CRADDOCKSTOWN, NAAS,
Co. KILDARE, [REDACTED]

Your nearest Broadband
Connection Point is
16.66 km >




Network Build in Progress

It's on the way! It is estimated that high speed Fibre Broadband will be available in your area within the date range above. To be the first to know when your area will be ready to connect, sign up.*

Anticipated date for connection: **April 2022 - June 2022**

[Get Local Updates](#)

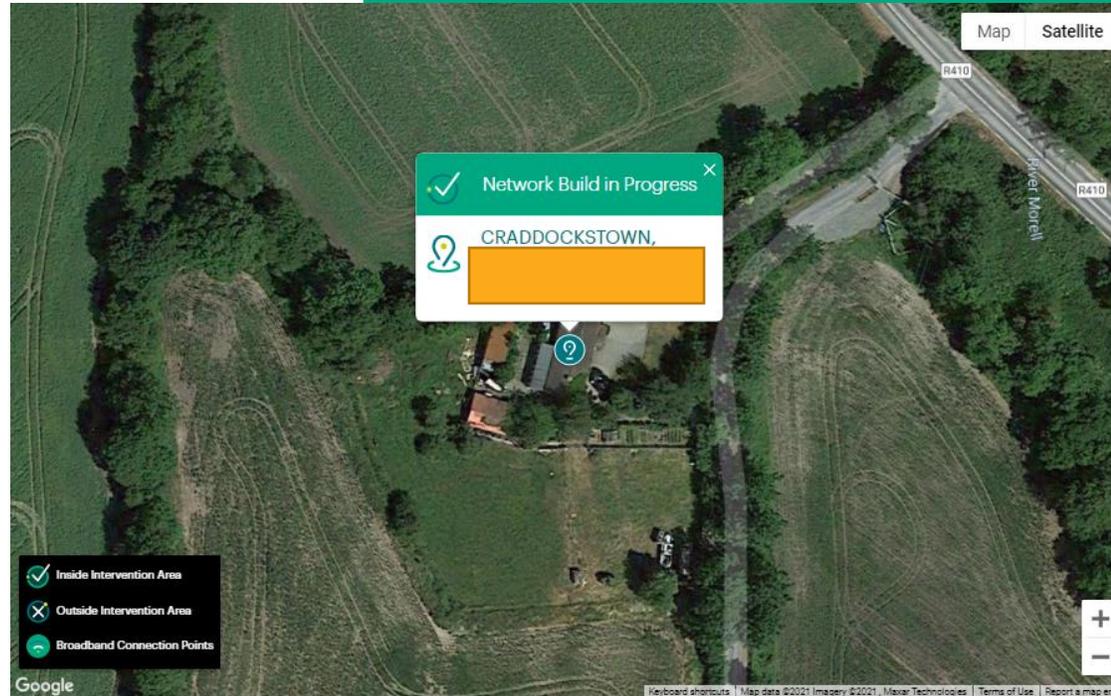

*All dates provided are estimated based on our current view, but are likely to change in the future.

For example, your premises may be re-assigned to another Deployment Area with a different rollout timescale. This Deployment Area reassignment can happen at any stage up until build is complete in the area. Other unforeseen changes outside the control of NBI can also impact the estimated date over the course of the rollout.

*All BCP's are subject to change. This may be due to unforeseen circumstances, or those outside of NBI's control.

BCP Search

Members of the public can easily determine where their nearest BCP is located.

www.nbi.ie/bcp-map/

Nearby Connection Points
Can't find your address?
Try moving the map.

- Seir Kieran Community Hall, OFFALY, R35 V124 18.63 km
- Ballycommon Telework and Training Centre, OFFALY, R35 V124 20.23 km
- Emo 'Old School' Community Centre, LAOIS, R32 KF74 21.86 km
- Rosfaraghan Business Park, OFFALY, R42 AX58 22.98 km
- Killavilla Community Centre, OFFALY, E53 FE42 23.45 km
- Kilclonfert Community Centre CLG, OFFALY, R35 T684 24.56 km
- Coolderry Community Hall, OFFALY, R42 DH05 25.07 km
- Fanure Community Hall, TIPPERARY, E53 AE02 26.10 km

Map Satellite

Connected
In Planning

Google

Keyboard shortcuts | Map data ©2021 Imagery ©2021 TerraMetrics | Terms of Use | Report a map error

* All BCPs are subject to change. This may be due to unforeseen circumstances, or those outside NBI's control.

Eircode Search Example – County Offaly

Want to learn more about Broadband Connection Points?

What is a BCP Find a BCP BCPs in schools

Search our network map

Search our BCP map to find your nearest Broadband Connection Point.


Offaly, County Offaly, Ireland

Don't know your Eircode? Find it using eircode.ie

Sign Up For Updates

The easiest way for members of the public to remain updated on the project status in their area is to **register on our website** to receive automatic updates.

www.nbi.ie/eoi

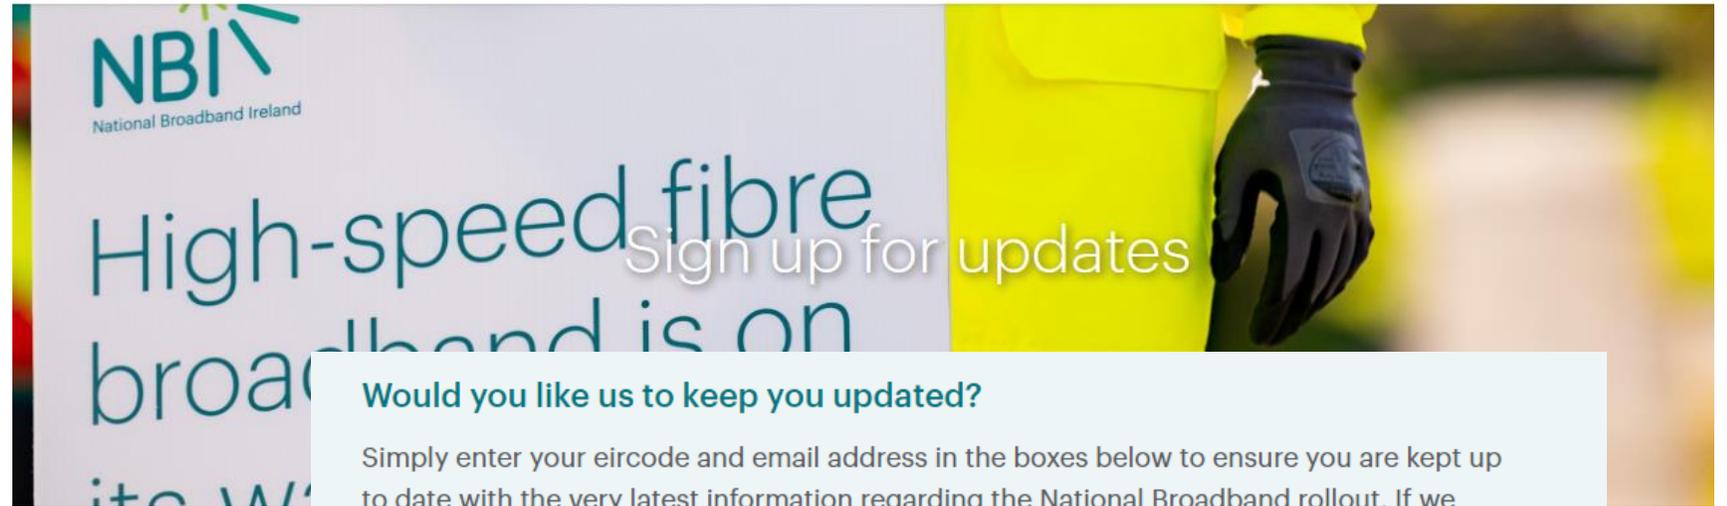

Would you like us to keep you updated?

Simply enter your eircode and email address in the boxes below to ensure you are kept up to date with the very latest information regarding the National Broadband rollout. If we have your details, we can contact you when service becomes available in your area.

<input type="text"/>	<input type="text"/>	<input type="text"/>
<input type="text"/>	<input type="button" value="KEEP UP TO DATE"/>	

NBI does not share or sell your personal information. Your data is strictly used within NBI group of companies for the purposes of the National Broadband Plan rollout. Please refer to our [Privacy Policy](#) for further information.


Interactive Deployment Area Map

A simple way to keep up to date and understand the status of different Deployment Areas, is to visit our [interactive map](#)

www.nbi.ie/where-are-we-working/

The map

- Is colour coded to see the various status of each Deployment Area
- Can zoom in to areas of interest
- Is clickable to reveal more details for that specific area

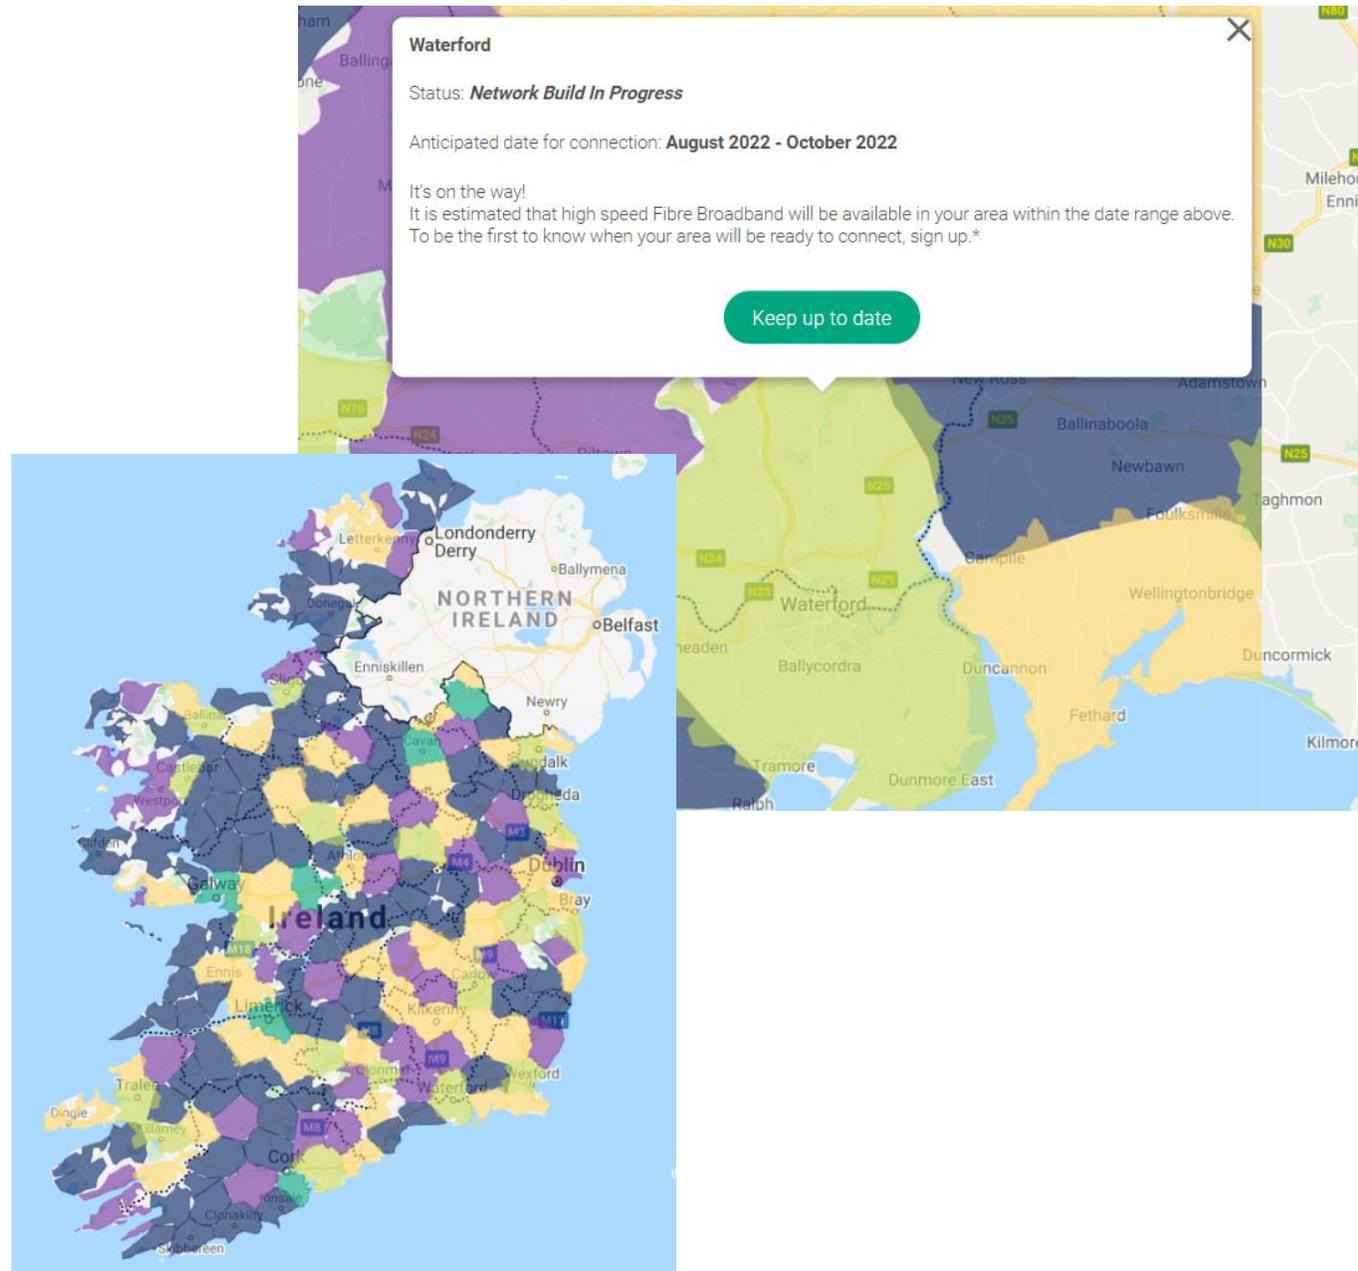


Not In the IA / Not Getting 30Mbps

If members of the public are not in the Intervention Area but still cannot get high speed broadband from broadband providers in their location, the Department of Communications has a process to review.

This review can potentially move premises from the “blue” part of the map to the “amber” part of the map.

Members of the public should contact the Department of Communications at broadband@decc.gov.ie to pursue this.

It would be helpful if members of the public could advise the Department of any operators, they may have contacted in relation to servicing their property.

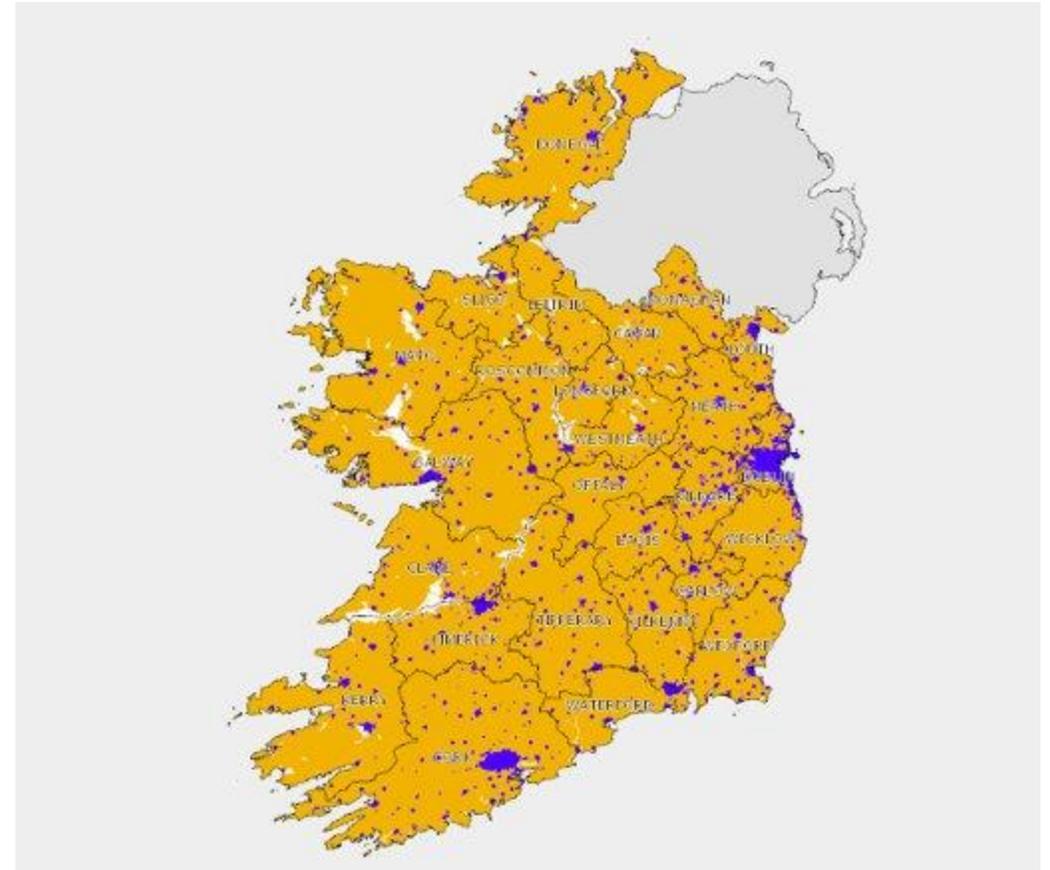

AMBER areas - the target areas for the State intervention of the National Broadband Plan.

BLUE areas - where commercial operators are delivering or have indicated plans to deliver high speed broadband services.

Sign up on www.nbi.ie
to keep up to date with developments in your area

Email for political reps: reps@nbi.ie

Contact us on: **0818 624 624**
email: contactus@nbi.ie



Rialtas
na hÉireann
Government
of Ireland

Tionscadal Éireann
Project Ireland
2040
